

TSML/FAPG/3379/FY223

Date:25/05/2022

To

The Chief Conservator of Forests (Central)
Eastern Regional Office
Ministry of Environment & Forests
Government of India
A/3, Chandrashekharapur,
Bhubaneswar - 751023, Odisha.

Sub: Half Yearly Compliance Report (October 2021 to March 2022) for Environmental Clearance to M/s Tata Steel Ltd. for 55,000 TPA High Carbon Ferro-Chrome Plant, at Gopalpur, Tehsil-Chhatrapur, District- Ganjam, Odisha.

Dear Sir,

We are enclosing the Half Yearly Compliance Report for the period October 2021 to March 2022 for the conditions stipulated in Environmental Clearance to the above referred project vide MoEF's letter No. J-11011/55/2011-IA.II(I) dated 14th August 2012 and amended EC dated 08th August 2014 & letter No. 11-63/2012-IA.III dated 18th March 2013 respectively for your kind consideration. The copy of the compliance report is also being sent in the soft format to e-mail id for your kind perusal.

We wish to mention that all the necessary actions are being taken in compliance to the specific and general conditions of Environmental Clearance granted to the project.

We trust that the information furnished is in line with your requirement.

Thanking You,
Yours faithfully,
For TATA STEEL Ltd.,



B Srinivas.
Factory Manager
Ferro Chrome Plant, Gopalpur
Tata Steel Limited

Encl. a/a

Copy to:

1. Member Secretary, State Pollution Control Board, Odisha, Bhubaneswar.
2. Regional Officer, State Pollution Control Board, Berhampur.



HALF YEARLY COMPLIANCE REPORT

Of

Environmental Clearance

(Period from October 2021 TO March 2022)

For

55,000 TPA High Carbon Ferro-Chrome Plant,

Of

M/s Tata Steel Limited

At- Gopalpur, Tehsil- Chhatrapur, District- Ganjam, Odisha

Half-Yearly Compliance Report (October 2021 to March 2022) of Environment Clearance Vide letter No. J-11011/55/2011-IA-II(I) dated 14.08.2012 and amendment of EC dated 08.08.2014 from MoEF for 55,000 TPA High Carbon Ferro Chrome Plant at Tehsil Chhatrapur, Ganjam, Odisha by TATA Steel Limited

Sl. No.	Specific Conditions	Compliance/Status
1	The proponent shall obtain necessary CRZ clearance under the provision of CRZ Notification, 2010	We have been granted CRZ Clearance under the provision of CRZ Notification, 2011 on 18.03.2013 vide letter no. F No. 11-63/2012-IA.III from MoEF&CC (IA Division).
2	No Charcoal shall be used as fuel. Pet Coal should be used as fuel instead of charcoal from unknown sources.	No Charcoal is used as fuel for plant operations.
3	Continuous monitoring facilities for all the stacks and sufficient air pollution control equipment viz. fume extraction system with bag filters, ID fan and stack of adequate height to submerged arc furnace shall be provided to control emission below 50 mg/Nm ³	<ul style="list-style-type: none"> • Installation of Continuous monitoring of SPM for process stacks in progress. • Fume Extraction System with bag filters and ID fan has been installed to control emission. • Adequate stack height is maintained in submerged arc furnace. • Dust extraction system also installed.
4	The National Ambient Air Quality Standards issued by the Ministry vide G.S.R. No. 826(E) dated 16 th November 2009 shall be followed.	NAAQ Standards have been referred for air quality monitoring and is being complied.
5	Secondary fugitive emissions from all the sources shall be controlled within the latest permissible limits issued by the Ministry and regularly monitored. Guidelines / Code of Practice issued by the CPCB shall be followed.	Water sprinkling on roads/operating areas is being carried out on a regular basis to control the fugitive emissions.
6	The total water requirement shall not exceed 5.5 MLD. 'Zero' effluent discharge shall be strictly followed, and no wastewater should be discharged outside the premises.	The water requirement for 55,000 TPA of Ferro Chrome Plant is 2000 KLD approx. The ETP and STP have been installed and no wastewater is discharged outside the premises.
7	Efforts shall be made to make use of rainwater harvested. If needed, capacity of the reservoir should be enhanced to meet the maximum water requirement. Only balance water requirement should be met from other sources.	The water reservoir of 6.5 lakhs KL capacity is also used to store the rainwater during the monsoon. Rainwater post treatment is used to meet the water requirement.
8	Regular monitoring of influent and effluent surface, sub-surface and ground water shall be ensured and treated wastewater shall meet the norms prescribed by the State Pollution Control Board or described under the Environment (Protection) Act whichever are more stringent. Leachate study for the effluent generated and analysis should also be regularly carried out and report submitted to the Ministry' Regional Office at Bhubaneswar, SPCB and CPCB.	<ul style="list-style-type: none"> • Surface water quality monitoring is being carried out regularly around the project site by third party registered and NABL accredited labs. • Upstream and downstream surface water is being carried out every month. Ground & Surface Water monitoring results is attached in Annexure-1.
9	All the Ferro chrome slag shall be used for land filling inside the plant or used as building material only after passing through Toxic Chemical Leachability Potential (TCLP) Test. Otherwise, hazardous substances shall be recovered from the slag and output waste and be disposed in secured landfill as per CPCB guidelines.	Ferro Chrome Slag testing for Toxic Chemical Leachability Potential (TCLP) has been done from IMMT. No hazardous substances found. The same can be used for landfill in low lying areas inside our plant premise.

Half-Yearly Compliance Report (October 2021 to March 2022) of Environment Clearance Vide letter No. J-11011/55/2011-IA-II(I) dated 14.08.2012 and amendment of EC dated 08.08.2014 from MoEF for 55,000 TPA High Carbon Ferro Chrome Plant at Tehsil Chhatrapur, Ganjam, Odisha by TATA Steel Limited

10	Risk and Disaster Management Plan along with the mitigation measures should be prepared and a copy submitted to the Ministry's Regional Office at Bhubaneswar, SPCB and CPCB within 3 months of issue of environment clearance letter.	Risk and Disaster Management Plan along with the mitigation measures have been submitted to the MoEF vide letter no. OP-Env/C-04/52/2012 dated 12.11.2012 along with a copy to Eastern Regional Office, MoEF and Odisha State Pollution Control Board, Bhubaneswar. Additionally, an onsite emergency plan approved by Directorate of Factories & Boilers is also in place.
11	All the commitments made to the public during the Public Hearing / Public Consultation meeting held on 20th September 2011 should be satisfactorily implemented and a separate budget for implementing the same should be allocated and information submitted to the Ministry's Regional Office at Bhubaneswar.	Commitments made to the public during Public hearing is being regularly implemented and monitored by Tata Steel Rural Development Society (TSRDS) within the allocated budget.
12	As proposed green belt should be developed in at least 33% of the project area. Selection of plant species shall be as per the CPCB guidelines in consultation with the DFO.	Green belt has been development has been taken up in phase wise manner. We planted over 52000 saplings with an average survival rate greater than 95%.
13	At least 5% of the total cost of the project should be earmarked towards the Enterprise Social Commitment based on Public Hearing issues and item-wise details along with time bound action plan should be prepared and submitted to the Ministry's Office at Bhubaneswar. Implementation of such program shall be ensured accordingly in a time bound manner.	<ul style="list-style-type: none"> Separate budget has been earmarked for the CSR activities, community as well as peripheral development activities such as Health, drinking water, Education, Environment etc. and is being done by our Tata Steel Rural Development Society wing. Rupees 383.74 lacs have been spent towards the above-mentioned activities in October 2020 to March 2021. (Refer Annexure-2)
14	The Company shall provide housing for construction labor within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, safe drinking water, medical health care, crèche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.	Necessary infrastructure & facilities for the construction labors was provided during the construction Work.
15	The Company shall submit within three months their policy towards Corporate Environment Responsibility which should inter-alia address (i) Standard operating process / procedure to being into focus any infringement/deviation/violation of environmental or forest norms/conditions, (ii) Hierarchical system or administrative order of the Company to deal with environmental issues and ensuring compliance to environmental clearance conditions and (iii) System of reporting of noncompliance/violation environmental norms to the Board of Directors of the company and/or stakeholders or shareholders.	The Corporate Environment Policy is in place and has been submitted to the MoEF&CC vide letter no. OP-Env/C-04/52/2012 dated 12.11.2012 with a copy to Regional Office, OSPCB.

Half-Yearly Compliance Report (October 2021 to March 2022) of Environment Clearance Vide letter No. J-11011/55/2011-IA-II(I) dated 14.08.2012 and amendment of EC dated 08.08.2014 from MoEF for 55,000 TPA High Carbon Ferro Chrome Plant at Tehsil Chhatrapur, Ganjam, Odisha by TATA Steel Limited

Sl. No.	General Conditions	Compliance/Status
1	The project authorities must strictly adhere to the stipulations made by the Orissa State Pollution Control Board and the State Government.	Stipulations as made by the State & Central Govt. are being adhered to from time to time.
2	No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment and Forests.	Amendment to Environmental Clearance was granted by MoEF&CC vide File no. J-11011/55/2011-IA II(I) on 08.08.2014.
3	The gaseous emissions from various process units shall conform to the load/mass-based standards notified by the Ministry on 19th May 1993 and standards prescribed from time to time. The State Board may specify more stringent standards for the relevant parameters keeping in view the nature of the industry and its size and location.	The Process units have the gaseous emissions under control and below the prescribed limits.
4	At least four ambient air quality monitoring stations should be established in the downward direction as well as where maximum ground level concentration of PM ₁₀ , SO ₂ and NOX are anticipated in consultation with the SPCB. Data on ambient air quality and stack emission shall be regularly submitted to this Ministry including its Regional Office at Bhubaneswar and the SPCB/CPCB once in six months.	Four ambient Air Quality & fugitive Emission monitoring stations installed. The ground level concentration of PM ₁₀ , SO ₂ and NOX etc. are as per the anticipation of SPCB. The Air Quality, Fugitive emission and Stack monitoring result is attached in Annexure-3 .
5	Industrial wastewater shall be properly collected, treated so as to conform to the standards prescribed under GSR 422(E) dated 19 th May 1993 and 31 st December 1993 or as amended from time to time. The treated wastewater shall be utilized for plantation purpose.	Industrial wastewater generated has been treated in Effluent Treatment Plant conforming to the standards and treated wastewater is recycled and re-used for green belt development, water sprinkling on roads, metal cooling activity etc.
6	The overall noise levels in and around the plant area shall be kept well within the standards (85dBA) by providing noise control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels should conform to the standards prescribed under EPA Rules, 1989 viz. 75 dBA (daytime) and 70 dBA (nighttime).	Ambient Noise monitoring is continuously monitored. Plant area is maintained within the standards. Noise Quality monitoring results is attached in Annexure-4 .
7	Occupational health surveillance of the workers shall be done on a regular basis and records maintained as per the Factories Act.	Health Records of the workers are being maintained as per Factories Act. Pre-Employment Medical check-up prior to the issue of their gate pass to work inside the site and Periodic Medical Check-up for the workers is being done.
8	The company shall develop surface water harvesting structures to harvest the rainwater for utilization in the lean season besides recharging the ground water table.	A water reservoir of 6.5 lakhs liter capacity is in place to store the rainwater post monsoon which will be used for plant operation post requisite treatment.

Half-Yearly Compliance Report (October 2021 to March 2022) of Environment Clearance Vide letter No. J-11011/55/2011-IA-II(I) dated 14.08.2012 and amendment of EC dated 08.08.2014 from MoEF for 55,000 TPA High Carbon Ferro Chrome Plant at Tehsil Chhatrapur, Ganjam, Odisha by TATA Steel Limited

9	<p>The project proponent shall also comply with all the environmental protection measures and safeguards recommended in the EIA/EMP report. Further, the company must undertake socio-economic development activities in the surrounding villages like community development programs, educational programs, drinking water supply and health care etc.</p>	<ul style="list-style-type: none"> • Environmental Protection measures as indicated in the EIA and EMP report has been implemented. • Socio-economic developmental activities in Health, Education, Sports, agriculture, and infrastructure development are being carried out in the surrounding and periphery villages.
10	<p>Requisite amount shall be earmarked towards capital cost and recurring cost/annum for environment pollution control measures to implement the conditions stipulated by the Ministry of Environment and Forests as well as the State Government. An implementation schedule for implementing all the conditions stipulated herein shall be submitted to the Regional Office of the Ministry at Bhubaneswar. The funds so provided shall not be diverted for any other purpose.</p>	<p>Separate budget has been earmarked towards capital and operating environment expenditure. Environment Annual Budget – Approx. Rs. 56,55,934/-</p>
11	<p>A copy of clearance letter shall be sent by the proponent to concern Panchayat, ZilaParishad/Municipal Corporation, Urban Local Body and the local NGO, if any, from whom suggestions/representations, if any, were received while processing the proposal. The clearance letter shall also be put on the web site of the company by the proponent.</p>	<ul style="list-style-type: none"> • Environment Clearance copy has been submitted to the concerned Govt. /Private Bodies in Aug 2012. • Environment Clearance letter has been uploaded on the Tata Steel website, www.tatasteel.com
12	<p>The project proponent shall upload the status of compliance of the stipulated environmental clearance conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent the Regional Office of the MoEF at Bhubaneswar. The respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM₁₀, SO₂, NO_x (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the projects shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.</p>	<ul style="list-style-type: none"> • Last six-monthly compliance reports have been uploaded to the company's website www.tatasteel.com. • Electronic multi-line display board installed to display the criteria pollutant levels namely; PM₁₀, SO₂, NO_x or critical sectoral parameters, indicated for the projects at main gate of the company for the public domain. • The compliance reports are being sent to the Regional Office, MoEF and the respective zonal office of CPCB and SPCB.
13	<p>The project proponent shall also submit six monthly reports on the status of the compliance of the stipulated environmental conditions including results of monitored data (both in hard copies as well as by e-mail) to the Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB. The Regional Office of this Ministry at Bhubaneswar/ CPCB/ SPCB shall monitor the stipulated conditions.</p>	<p>Last Six-Monthly Compliance report for the period October'2021 to March'2022 was submitted to MoEF/OSPCB Regional Office both in hard as well as soft copy in November2021.</p>

Half-Yearly Compliance Report (October 2021 to March 2022) of Environment Clearance Vide letter No. J-11011/55/2011-IA-II(I) dated 14.08.2012 and amendment of EC dated 08.08.2014 from MoEF for 55,000 TPA High Carbon Ferro Chrome Plant at Tehsil Chhatrapur, Ganjam, Odisha by TATA Steel Limited

14	The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of environmental conditions and shall also be sent to the respective Regional Office of the MoEF at Bhubaneswar by e-mail.	The environmental statement has been submitted every year and the same has been uploaded on company's website www.tatasteel.com .
15	The Project Proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the SPCB and may also be seen at Website of the Ministry of Environment and Forests at http://envfor.nic.in . This shall be advertised within seven days from the date of issue of the clearance letter, at least in two local newspapers that are widely circulated in the region of which one shall be in the vernacular language of the locality concerned and a copy of the same should be forwarded to the Regional Office at Bhubaneswar.	Complied. Paper advertisement details are as follows; a. Odia: SAMBAD, Page No. 9 b. English: The New Indian Express, Page no. 5 Advertisement details have been submitted to the MoEF Eastern Regional Office at Bhubaneswar on 19.08.12 and were also attached with the 1 st Half Yearly Compliance Report.
16	Project authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of commencing the land development work.	<ul style="list-style-type: none"> • Project received final approval from Tata Steel Board in August 2010 and is being funded through internal accruals. • Ground leveling activities was started on 04.05.2013 and the same was being intimated to the board vide letter no PG-Env/C-01/03/2013 & PG-Env/C-01/04/2013, dated 10th May 2013. However, frequent strikes by the local people have deferred the plant operation.



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2339

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022

SURFACE WATER QUALITY ANALYSIS REPORT

Annexure-1

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur

2. Sampling Location : SW1- Khara Nalla Upstream

Sl. No	Parameter	Unit	Standards as per IS-2296:1992 Class -'C'	OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	Six Monthly Averages
1	Colour (max)	Hazen	300	<5	<5	<5	<5	<5	<5	<5
2	pH Value at 25 ^o C	--	6.0-9.0	7.56	7.9	7.9	8.7	8.2	8.18	8.1
3	Dissolved Oxygen (minimum)	mg/l	4.0	6.6	6.2	6.2	6.6	6.3	6.6	6.4
4	Chloride (max)	mg/l	600	114	17	17	18	24	28	36.3
5	Total Dissolved Solids	mg/l	1500	460	187	187	192	349	351	287.7
6	BOD (3) days at 27 ^o C (max)	mg/l	3.0	BDL	BDL	BDL	BDL	BDL	<1	<1
7	Arsenic as As	mg/l	0.2	BDL	BDL	BDL	BDL	BDL	<0.004	<0.004
8	Lead as Pb(max)	mg/l	0.1	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
9	Cadmium as Cd (max)	mg/l	0.01	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
10	Hexavalent Chromium as Cr ⁺⁶	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
11	Copper as Cu (max)	mg/l	1.5	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
12	Zinc as Zn(max)	mg/l	15	BDL	BDL	BDL	BDL	BDL	<0.03	<0.03
13	Selenium as Se (max)	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.001	<0.001
14	Cyanide as CN (max)	mg/l	0.05	ND	ND	ND	ND	ND	<0.01	<0.01
15	Fluoride as F (max)	mg/l	1.5	0.39	0.94	0.94	0.91	0.88	<0.1	0.8
16	Sulphates (SO ₄) (max)	mg/l	400	72	2.8	2.8	3.2	3.1	3.8	14.6
17	Phenolic Compounds as C ₆ H ₅ OH (max)	mg/l	0.005	BDL	BDL	BDL	BDL	BDL	<0.05	<0.05
18	Iron as Fe (max)	mg/l	0.5	0.79	1.02	1.02	1.18	1.24	1.22	1.1
19	Nitrate as NO ₃ , (max)	mg/l	50	7.9	12.6	12.6	13.4	13.8	11.8	12.0
20	Anionic Detergents (max)	mg/l	1.0	ND	ND	ND	ND	ND	<0.2	<0.2
21	Total Coli form	MPN/100	5000	1440	1660	1660	1620	1580	1600	1593.3
22	Cadmium	mg/l	0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
23	Zinc as Zn	mg/l	15	<0.5	<0.5	<0.5	<0.5	<0.5	<0.03	<0.03
24	Oil & Grease	mg/l	0.1	ND	ND	ND	ND	ND	<0.5	<0.5
25	Fecal Coliform	MPN/100	--	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8

Reviewed By



Manoj

Approved By

Puja Mohanty





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2340

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 SURFACE WATER QUALITY ANALYSIS REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : SW2-Khara Nalla Downstream

Sl. No	Parameter	Unit	Standards as per IS-2296:1992 Class -'C'	OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	Six Monthly Averages
1	Colour (max)	Hazen	300	5	5	5	5	5	5	5
2	pH Value at 25° C	--	6.0-9.0	7.84	7.91	7.91	9.1	8.21	8.26	8.2
3	Dissolved Oxygen (minimum)	mg/l	4.0	7.2	6.8	6.8	6.9	6.4	6.8	6.8
4	Chloride (max)	mg/l	600	58	19	19	24	28	32	30.0
5	Total Dissolved Solids	mg/l	1500	198	184	184	188	432	440	271.0
6	BOD (3) days at 27°C (max)	mg/l	3.0	BDL	BDL	BDL	BDL	BDL	<1	<1
7	Arsenic as As	mg/l	0.2	BDL	BDL	BDL	BDL	BDL	<0.004	<0.004
8	Lead as Pb(max)	mg/l	0.1	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
9	Cadmium as Cd (max)	mg/l	0.01	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
10	Hexavalent Chromium as Cr ⁺⁶	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
11	Copper as Cu (max)	mg/l	1.5	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
12	Zinc as Zn(max)	mg/l	15	BDL	BDL	BDL	BDL	BDL	<0.03	<0.03
13	Selenium as Se (max)	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.001	<0.001
14	Cyanide as CN (max)	mg/l	0.05	ND	ND	ND	ND	ND	<0.01	<0.01
15	Fluoride as F (max)	mg/l	1.5	0.28	0.018	0.018	0.021	0.018	<0.1	0.1
16	Sulphates (SO ₄) (max)	mg/l	400	9.8	4.4	4.4	4.8	4.2	4.4	5.3
17	Phenolic Compounds as C ₆ H ₅ OH (max)	mg/l	0.005	BDL	BDL	BDL	BDL	BDL	<0.05	<0.05
18	Iron as Fe (max)	mg/l	0.5	0.39	1.54	1.54	1.62	1.68	1.74	1.4
19	Nitrate as NO ₃ (max)	mg/l	50	3.8	11.8	11.8	12.8	13.1	12.4	11.0
20	Anionic Detergents (max)	mg/l	1.0	ND	ND	ND	ND	ND	<0.2	<0.2
21	Total Coli form	MPN/100	5000	1148	1220	1220	1240	1260	1240	1221.3
22	Cadmium	mg/l	0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
23	Zinc as Zn	mg/l	15	<0.5	<0.5	<0.5	<0.5	<0.5	<0.03	<0.03
24	Oil & Grease	mg/l	0.1	ND	ND	ND	ND	ND	<0.5	<0.5
25	Fecal Coliform	MPN/100	--	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8



Reviewed By

M. Panda

Pooja Mohanty



Approved By



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2341

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022

SURFACE WATER QUALITY ANALYSIS REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : SW3-Reservoir

Sl. No	Parameter	Unit	Standards as per IS-2296:1992 Class -'C'	OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	Six Monthly Averages
1	Colour (max)	Hazen	300	<5	<5	<5	<5	<5	<5	<5
2	pH Value at 25 ^o C	--	6.0-9.0	8.24	8	8	8.2	8.23	8.31	8.2
3	Dissolved Oxygen (minimum)	mg/l	4.0	6.8	6.6	6.6	6.4	6.1	6.4	6.5
4	Chloride (max)	mg/l	600	42	16	16	18	24	26	23.7
5	Total Dissolved Solids	mg/l	1500	324	169	169	174	410	398	274
6	BOD (3) days at 27 ^o C (max)	mg/l	3.0	BDL	BDL	BDL	BDL	BDL	<1	<1
7	Arsenic as As	mg/l	0.2	BDL	BDL	BDL	BDL	BDL	<0.004	<0.004
8	Lead as Pb(max)	mg/l	0.1	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
9	Cadmium as Cd (max)	mg/l	0.01	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
10	Hexavalent Chromium as Cr ⁺⁶	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.01	<0.01
11	Copper as Cu (max)	mg/l	1.5	BDL	BDL	BDL	BDL	BDL	<0.02	<0.02
12	Zinc as Zn(max)	mg/l	15	BDL	BDL	BDL	BDL	BDL	<0.03	<0.03
13	Selenium as Se (max)	mg/l	0.05	BDL	BDL	BDL	BDL	BDL	<0.001	<0.001
14	Cyanide as CN (max)	mg/l	0.05	ND	ND	ND	ND	ND	<0.01	<0.01
15	Fluoride as F (max)	mg/l	1.5	0.44	1.8	1.8	2.1	2.8	3.2	2.0
16	Sulphates (SO ₄) (max)	mg/l	400	9.4	6.8	6.8	7.2	7.91	8.28	7.7
17	Phenolic Compounds as C ₆ H ₅ OH (max)	mg/l	0.005	<0.001	<0.001	<0.001	<0.001	<0.001	<0.05	<0.05
18	Iron as Fe (max)	mg/l	0.5	0.71	0.84	0.84	0.88	0.89	0.46	0.77
19	Nitrate as NO ₃ (max)	mg/l	50	4.2	5.4	5.4	5.4	5.8	5.8	5.3
20	Anionic Detergents (max)	mg/l	1.0	ND	ND	ND	ND	ND	<0.2	<0.2
21	Total Coli form	MPN/100 ml	5000	1266	1460	1460	1466	1508	1400	1426.7
22	Cadmium	mg/l	0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
23	Zinc as Zn	mg/l	15	<0.5	<0.5	<0.5	<0.5	<0.5	<0.03	<0.03
24	Oil & Grease	mg/l	0.1	ND	ND	ND	ND	ND	<0.5	<0.5
25	Fecal Coliform	MPN/100 ml	--	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8	<1.8



Reviewed By

Manda

Puja Mohanty



Approved By

Annexure-2

CSR Expenditure by Tata Steel, Gopalpur during October'21 to March'22		
Sl. No.	Expenditure Head	Amount (in lakhs)
1	Drinking water	0.51
2	Health	19.34
3	Education	14.97
4	Skill Development	48.00
5	Agriculture	116.34
6	Empowerment	23.70
7	Environment	1.47
8	Sports	0.78
9	Infrastructure	10.79
10	Special Commitments	114.29
11	Common Exp./Administration	17.84
12	COVID-19	15.72
13	Model School	0.00
14	TOTAL	383.74



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2331

Date :05.04.2022

Annexure-3

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 AAQ MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : AAQ-1 : MRSS Building Roof

AAQ-1: MRSS Building Roof	PM ₁₀ (µg/m ³)	PM _{2.5} (µg/m ³)	SO ₂ (µg/m ³)	NO _x (µg/m ³)	NH ₃ (µg/m ³)	O ₃ (µg/m ³)	CO (mg/m ³)	Pb (µg/m ³)	Ni (ng/m ³)	As (ng/m ³)	C ₆ H ₆ (µg/m ³)	BaP (ng/m ³)
Limit as per CPCB Notification, New Delhi, 18 th Nov 2009 For Ambient Air Quality	100	60	80	80	400	100	4	1	50	5	1	6
October-21	53.7	32.2	11.6	12.7	BDL	0.51	BDL	BDL	BDL	BDL	BDL	BDL
November -21	59.5	35.7	12.1	14.4	BDL	0.65	BDL	BDL	BDL	BDL	BDL	BDL
December -21	61.5	36.9	12.8	15.3	BDL	0.67	BDL	BDL	BDL	BDL	BDL	BDL
January -22	63.7	38.2	13.4	16.2	BDL	0.70	BDL	BDL	BDL	BDL	BDL	BDL
February-22	65.5	39.3	13.8	16.6	BDL	0.69	BDL	BDL	BDL	BDL	BDL	BDL
March -22	70.3	42.2	14.7	18.2	BDL	0.78	BDL	BDL	BDL	BDL	BDL	BDL
Annual Averages	62.4	37.4	13.1	15.6	BDL	0.67	BDL	BDL	BDL	BDL	BDL	BDL



Reviewed By

M. Panda

Puja Mohanty



Approved By





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

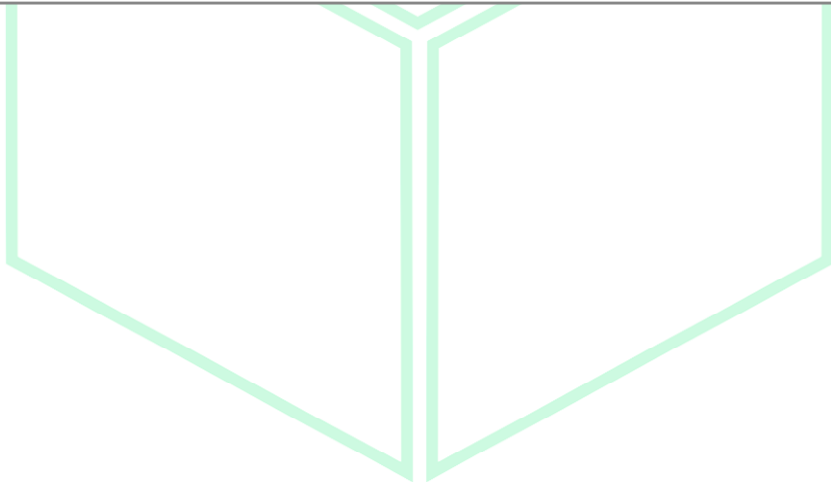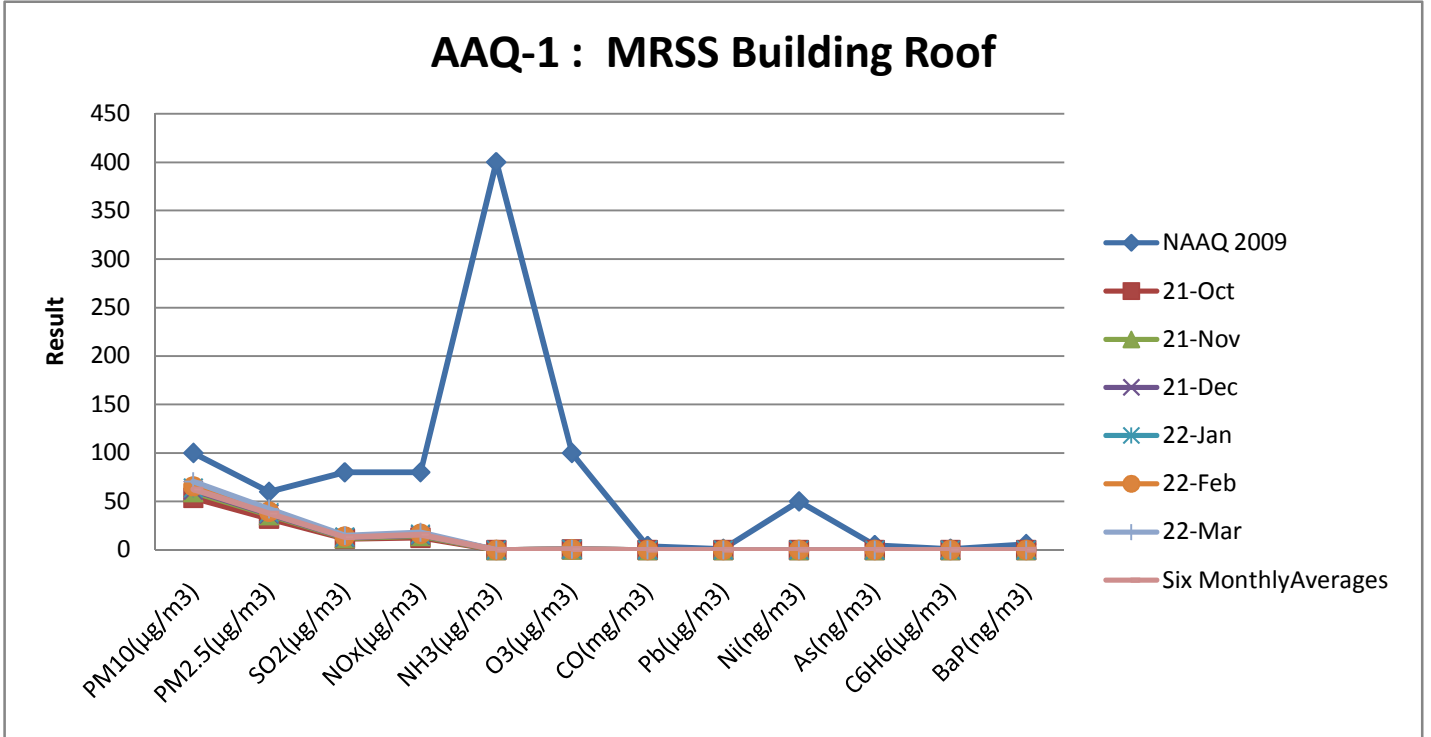



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2332

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 AAQ MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : AAQ-2 : LBSS Building Roof

AAQ-1: MRSS Building Roof	PM ₁₀ (µg/m ³)	PM _{2.5} (µg/m ³)	SO ₂ (µg/m ³)	NO _x (µg/m ³)	NH ₃ (µg/m ³)	O ₃ (µg/m ³)	CO (mg/m ³)	Pb (µg/m ³)	Ni (ng/m ³)	As (ng/m ³)	C ₆ H ₆ (µg/m ³)	BaP (ng/m ³)
Limit as per CPCB Notification, New Delhi, 18 th Nov 2009 For Ambient Air Quality	100	60	80	80	400	100	4	1	50	5	1	6
October-21	61.4	36.8	8.2	11.1	BDL	0.5	BDL	BDL	BDL	BDL	BDL	BDL
November -21	63.2	37.9	9.1	12.8	BDL	0.69	BDL	BDL	BDL	BDL	BDL	BDL
December -21	69.1	41.5	9.2	13.1	BDL	0.71	BDL	BDL	BDL	BDL	BDL	BDL
January -22	72.5	43.5	10.2	13.4	BDL	0.79	BDL	BDL	BDL	BDL	BDL	BDL
February-22	72.1	43.2	9.6	15.9	BDL	0.80	BDL	BDL	BDL	BDL	BDL	BDL
March -22	74.0	44.4	9.8	15.8	BDL	0.70	BDL	BDL	BDL	BDL	BDL	BDL
Annual Averages	68.7	41.2	9.4	13.7	BDL	0.70	BDL	BDL	BDL	BDL	BDL	BDL



Reviewed By

M. Anand



Approved By

Puja Mohanty





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

AAQ-2 : LBSS Building Roof

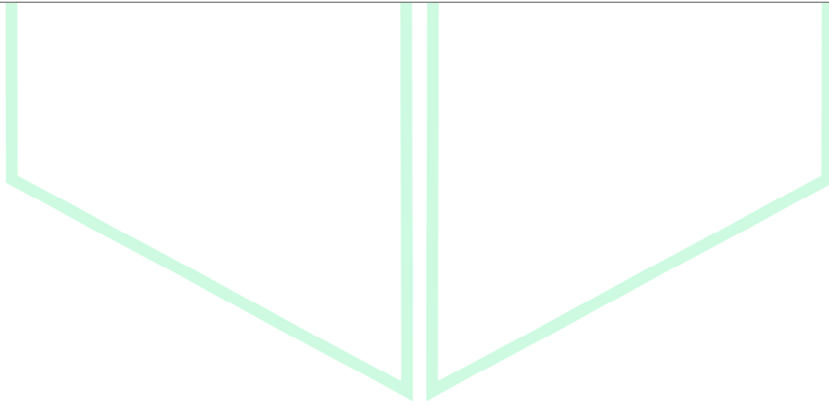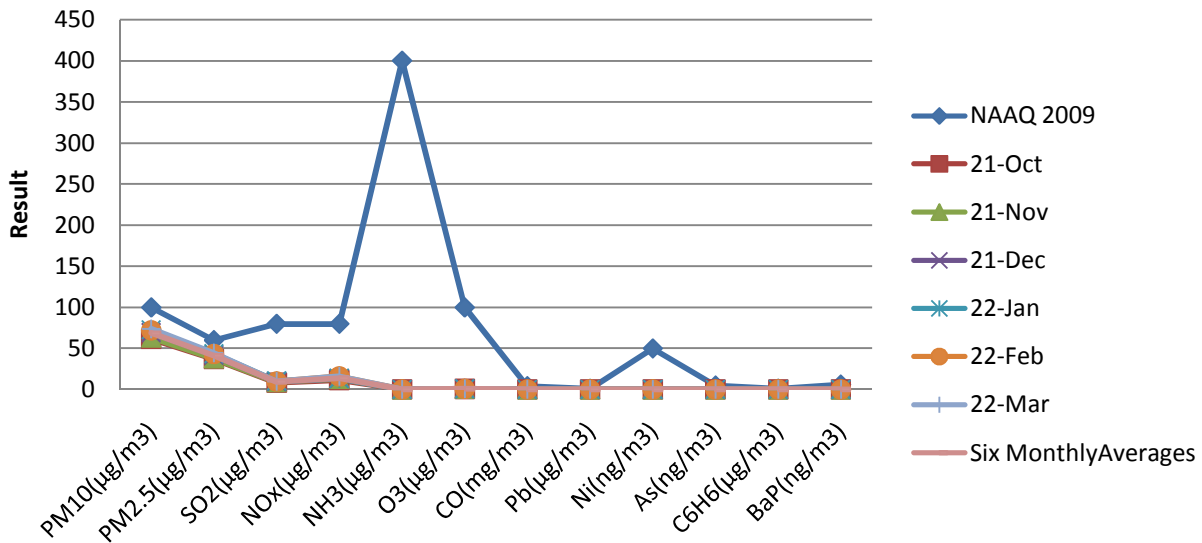



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2333

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 AAQ MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : AAQ-3 : Canteen Building Roof

AAQ-1: MRSS Building Roof	PM ₁₀ (µg/m ³)	PM _{2.5} (µg/m ³)	SO ₂ (µg/m ³)	NO _x (µg/m ³)	O ₃ (µg/m ³)	CO (mg/m ³)	NH ₃ (µg/m ³)	C ₆ H ₆ (µg/m ³)	BaP (ng/m ³)	Ni (ng/m ³)	Pb (µg/m ³)	As (ng/m ³)
Limit as per CPCB Notification, New Delhi, 18 th Nov 2009 For Ambient Air Quality	100	60	80	80	180	4	400	5	1	20	1	6
October-21	56.4	33.9	10.5	12.7	BDL	0.51	BDL	BDL	BDL	BDL	BDL	BDL
November -21	61.7	37.0	9.8	12.6	BDL	0.59	BDL	BDL	BDL	BDL	BDL	BDL
December -21	62.4	37.4	10.2	13.7	BDL	0.60	BDL	BDL	BDL	BDL	BDL	BDL
January -22	65.3	39.2	10.8	13.6	BDL	0.62	BDL	BDL	BDL	BDL	BDL	BDL
February-22	65.9	39.5	11.7	14.8	BDL	0.71	BDL	BDL	BDL	BDL	BDL	BDL
March -22	71.6	43.0	11.0	15.4	BDL	0.62	BDL	BDL	BDL	BDL	BDL	BDL
Annual Averages	63.9	38.3	10.7	13.8	BDL	0.61	BDL	BDL	BDL	BDL	BDL	BDL



Reviewed By

M. Anand

Puja Mohanty



Approved By





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

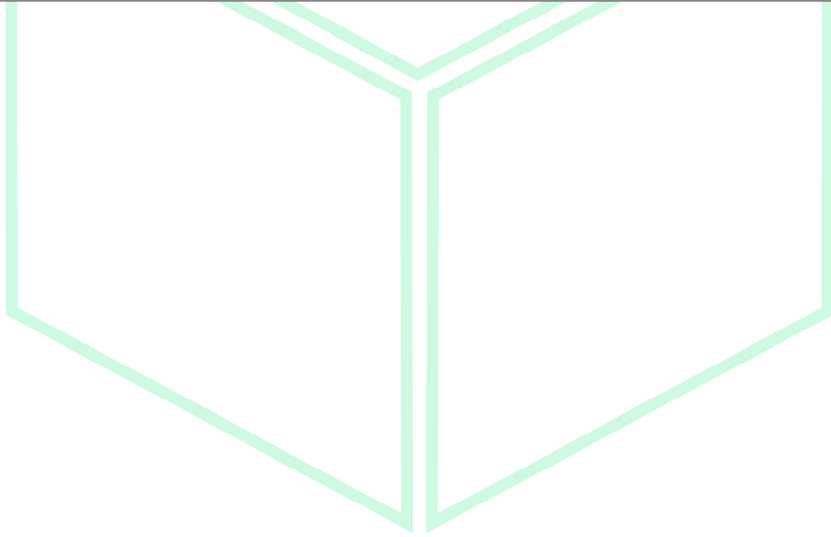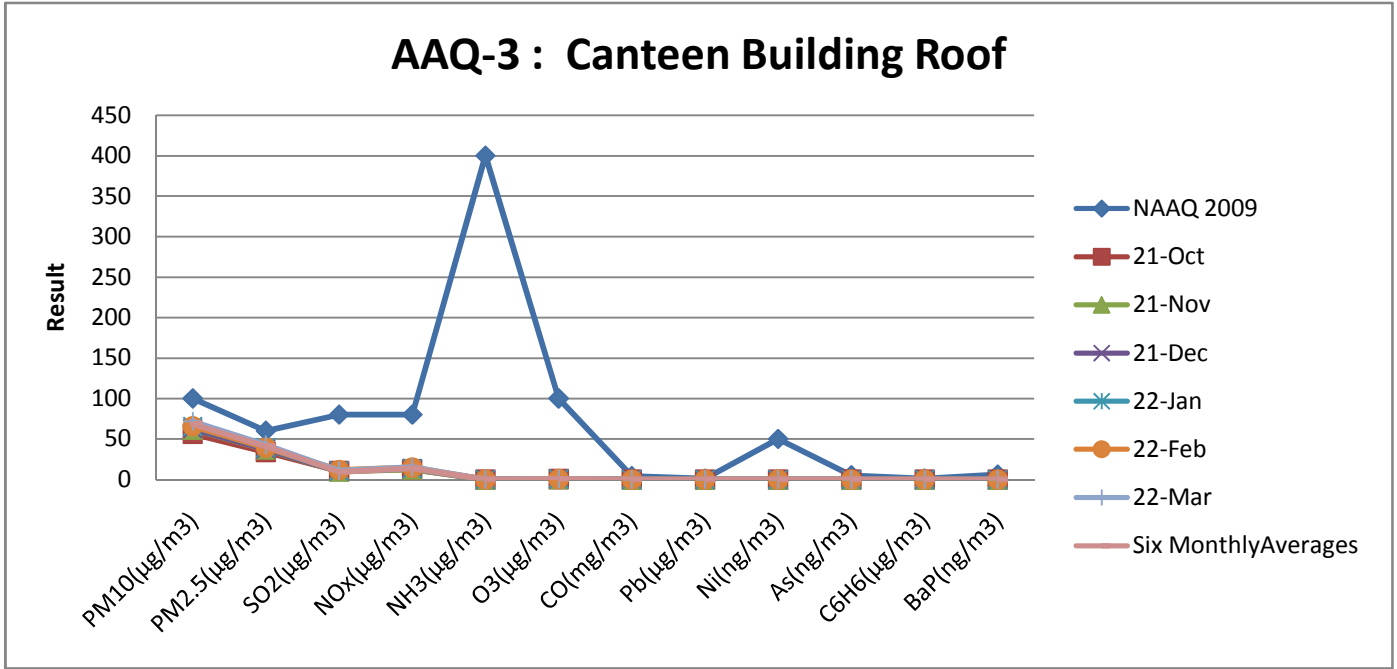



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2334

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 AAQ MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : AAQ-4 : ETP Building Roof

AAQ-1: MRSS Building Roof	PM ₁₀ (µg/m ³)	PM _{2.5} (µg/m ³)	SO ₂ (µg/m ³)	NO _x (µg/m ³)	NH ₃ (µg/m ³)	O ₃ (µg/m ³)	CO (mg/m ³)	Pb (µg/m ³)	Ni (ng/m ³)	As (ng/m ³)	C ₆ H ₆ (µg/m ³)	BaP (ng/m ³)
Limit as per CPCB Notification, New Delhi, 18 th Nov 2009 For Ambient Air Quality	100	60	80	80	400	100	4	1	50	5	1	6
October-21	64.3	38.6	9.1	13	BDL	0.54	BDL	BDL	BDL	BDL	BDL	BDL
November -21	71.8	43.1	10.3	13.6	BDL	0.67	BDL	BDL	BDL	BDL	BDL	BDL
December -21	65.5	39.3	12.5	15.6	BDL	0.6	BDL	BDL	BDL	BDL	BDL	BDL
January -22	70.9	42.6	12.6	15.4	BDL	0.64	BDL	BDL	BDL	BDL	BDL	BDL
February-22	65.2	39.1	11.8	17.2	BDL	0.71	BDL	BDL	BDL	BDL	BDL	BDL
March -22	67.1	40.3	12.4	15.6	BDL	0.73	BDL	BDL	BDL	BDL	BDL	BDL
Annual Averages	67.5	40.5	11.5	15.1	BDL	0.65	BDL	BDL	BDL	BDL	BDL	BDL



Reviewed By

Manda



Approved By

Pooja Mohanty





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

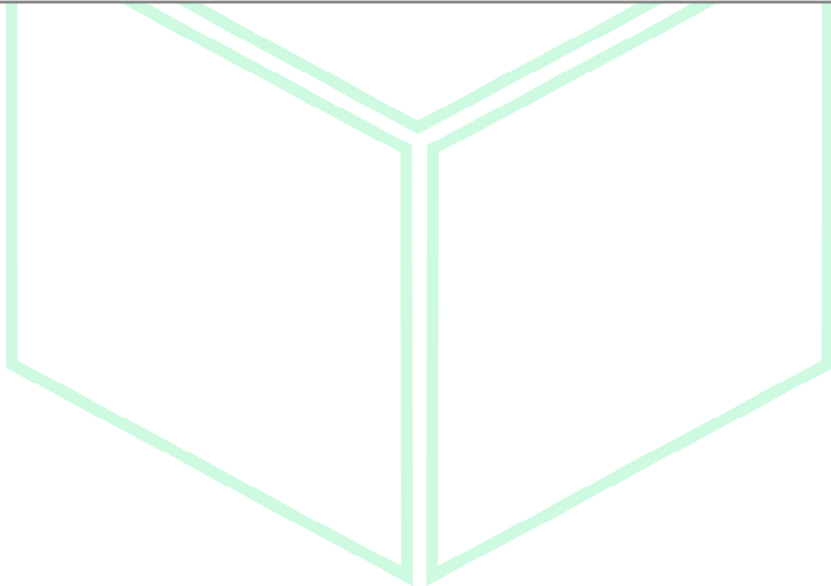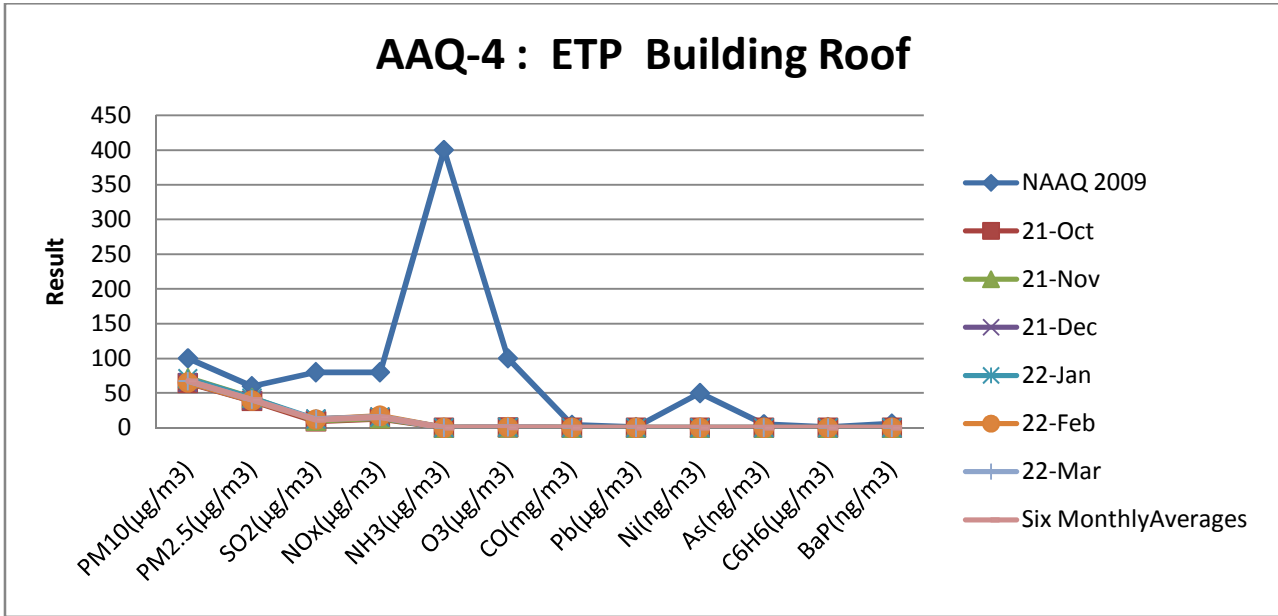



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services


Ref : Envlab/22/R-2335

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 FUGITIVE EMISSION MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur

Month	Particulate Matter ($\mu\text{g}/\text{m}^3$)		
	F-1: RMHS (Raw Material Handling Site)	F-2: FPHS (Fine Product Handling Site)	F-3: I- Bin Building
October -21	591	549	571
November-21	594	551	566
December-21	611	558	594
January-22	615	564	602
February-22	621	581	608
March-22	624	588	614
Six Monthly Averages	609.3	565.2	592.5
MoEF & CC Norms	1200 $\mu\text{g}/\text{m}^3$		

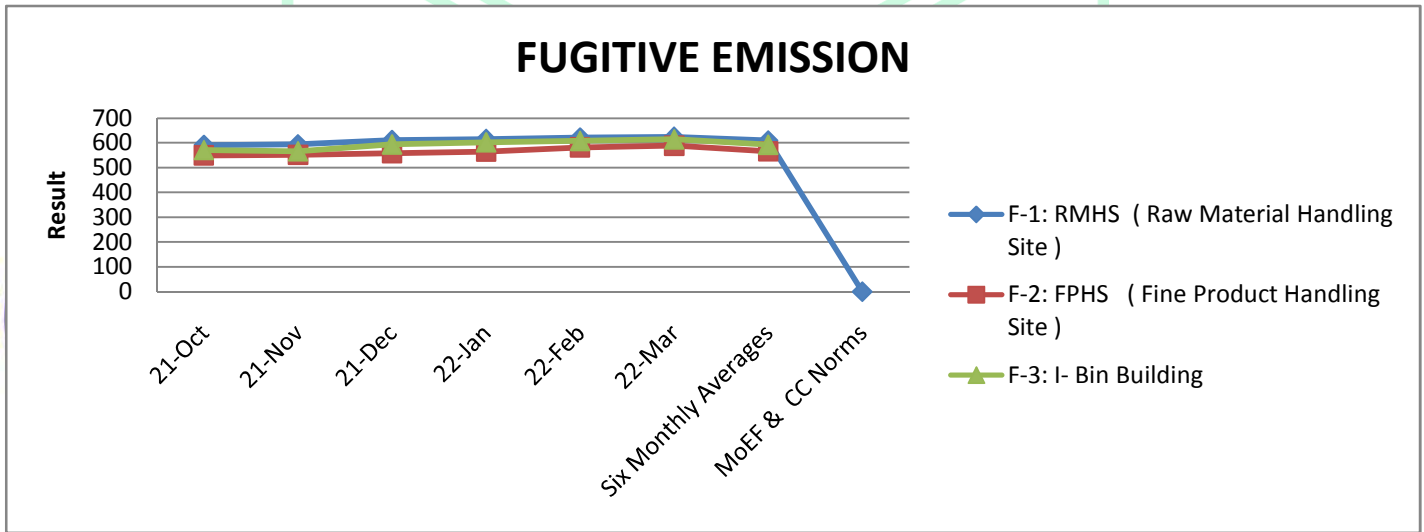

Reviewed By



Approved By





- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2337

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 STACK QUALITY MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur
2. Sampling Location : ST1: GCP-I

ST1_ GCP Bag Filter	OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	Six Monthly Averages
Stack Temperature	57	53	54	56	58	62	56.7
Velocity of Flue Gas	14.26	12.96	12.34	13.82	14.26	13.66	13.6
Quantity of Gas flow	128361.2	131416.2	129566.8	134422.6	128613	132466	130807.6
Concentration of Particulate Matter as PM	25.6	28.4	29.6	27.8	28.8	29.1	28.2
Sulphur dioxide as SO ₂	17.8	18.4	19.2	18.8	19.6	20.2	19.0
Oxides of Nitrogen as NO _x	18.8	19.2	19.8	20.6	23.8	24.6	21.1



Reviewed By

Manda



Approved By

Puja Mohanty



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2338

Date :05.04.2022

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 STACK QUALITY MONITORING REPORT

1. Name of Industry : **M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur**
2. Sampling Location : **ST2: GCP-2**

ST1_GCP Bag Filter	OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	Six Monthly Averages
Stack Temperature	110	111	118	124	128	110	116.8
Velocity of Flue Gas	19.44	15.9	16.4	13.8	13.04	8.33	14.5
Quantity of Gas flow	148512.38	152186.91	152892.94	154996.28	151212	113991	145632.0
Concentration of Particulate Matter as PM	39.8	34.9	35.6	36.8	31.4	22.4	33.5
Sulphur dioxide as SO ₂	23.8	22.6	23.8	24.6	22.8	20.6	23.0
Oxides of Nitrogen as NO _x	27.4	28.2	28.6	26.8	27.4	23.4	27.0




Reviewed By

M. Panda



Approved By

Puja Mohanty

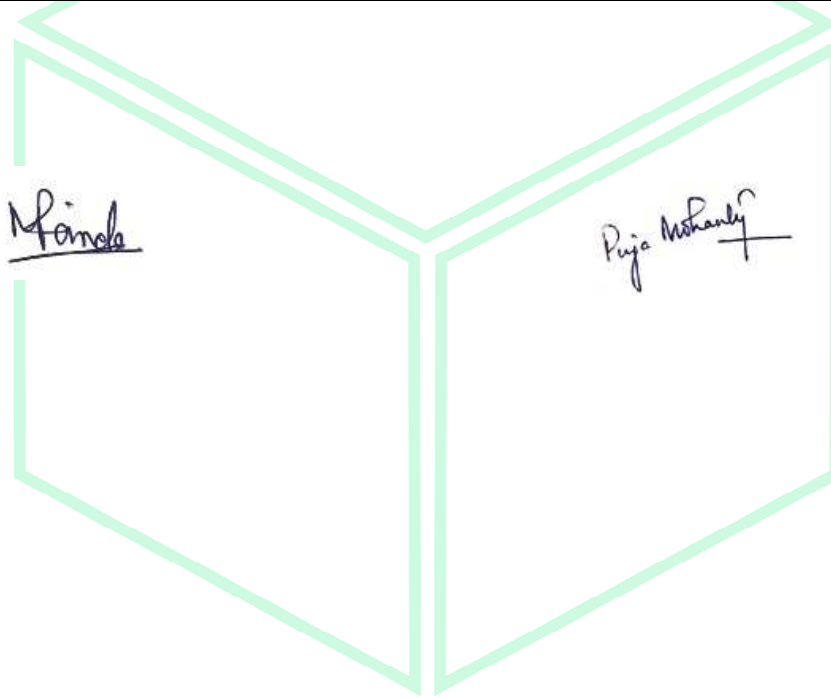



- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

Ref : Envlab/22/R-2336

Date :05.04.2022

Annexure-4

SIX MONTHLY COMPLIANCE REPORT FROM OCT 2021 TO MAR 2022 NOISE MONITORING REPORT

1. Name of Industry : M/s. TATA Steel Ltd, (Ferro Chrome Plant), Gopalpur

Location ID	Ambient Noise Monitoring Station Location	Day Time Equivalent Noise Level in dB(A) Leq						Six Monthly Averages
		OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	
N1	MRSS	59.6	60.8	62.6	63.8	64.8	66.8	63.1
N2	LBSS	58.4	61.9	63.8	64.6	65.2	63.6	62.9
N3	CANTEEN	58.1	62.6	64.6	63.2	62.8	61.8	62.2
N4	ETP	59.4	63.4	65.2	66.8	64.6	62.7	63.7
Standard as per CPCB		75						

Location ID	Ambient Noise Monitoring Station Location	Night Time Equivalent Noise Level in dB(A) Leq						Six Monthly Averages
		OCT-21	NOV-21	DEC-21	JAN-22	FEB-22	MAR-22	
N1	MRSS	50.6	55.8	56.8	58.4	59.2	59.8	56.8
N2	LBSS	46.8	49.2	52.2	53.9	51.8	53.4	51.2
N3	CANTEEN	47.4	48.8	51.4	53.6	52.8	53.2	51.2
N4	ETP	47.2	51.4	52.2	54.8	53.9	54.1	52.3
Standard as per CPCB		70						



M. Panda

Puja Mohanty



Approved By




- Infrastructure Engineering
- Water Resource Management
- Environmental & Social Study

- Surface & Sub-Surface Investigation
- Quality Control & Project Management
- Renewable Energy

- Agricultural Development
- Information Technology
- Public Health Engineering

- Mine Planning & Design
- Mineral/Sub-Soil Exploration
- Waste Management Services

NOISE DATA (DAY TIME)

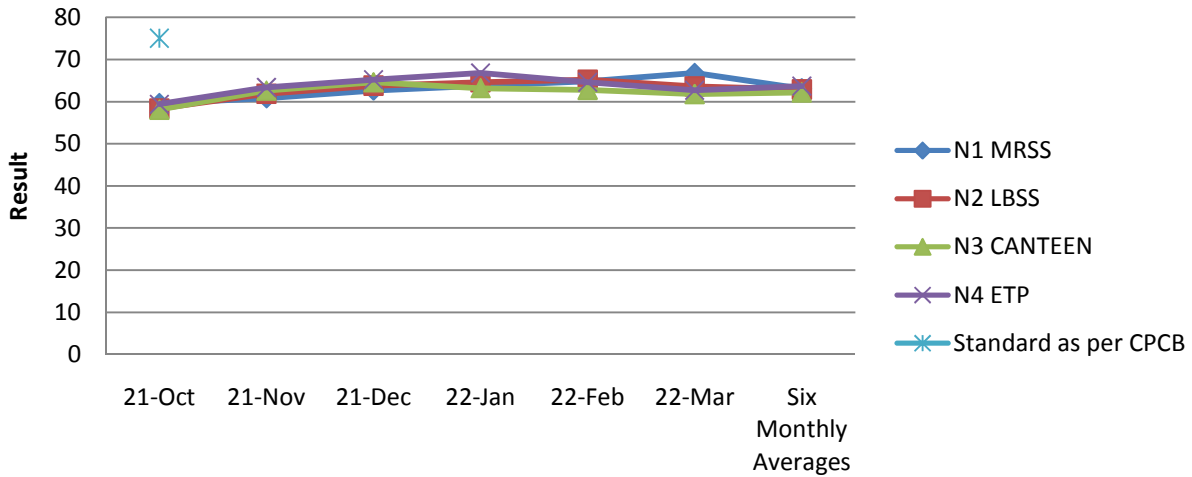

NOISE DATA (NIGHT TIME)

